



ERP Survival Guide

Mastering NetSuite Implementation

7 strategies to evaluate, decide,
and implement with confidence



Choosing and implementing an enterprise resource planning (ERP) system is one of the most consequential decisions an organization can make. Whether you are still evaluating your options or have already selected the NetSuite platform and are ready to begin implementation, the strategies in this guide are designed for you.

The NetSuite ERP platform has established itself as a leading cloud ERP solution, trusted by thousands of organizations across industries, from wholesale distribution and professional services to software companies and discrete manufacturers. Its strength lies in a unified architecture that connects financials, operations, supply chain, and customer management in a single system. But that strength only materializes when the platform is the right fit and is implemented with discipline.

This guide offers seven practical strategies built around a simple truth: Technology does not transform organizations. People and decisions do. The platform is the enabler, but the work is yours.

At Crowe, we help organizations navigate both the decision and the journey by combining deep NetSuite expertise with industry knowledge to deliver implementations that hold up over time.

1

Select the right tool for the job

The NetSuite platform might be the right core solution, but it is rarely the only tool an organization needs. Acknowledging that upfront is not a weakness. Instead, it is a sign of clear thinking.

ERP platforms are designed to manage the core of business: financial transactions, inventory, order management, procurement, and reporting. However, they are not always the best fit for every adjacent function. A manufacturer running complex production scheduling might need a dedicated planning tool alongside the NetSuite platform. A professional services firm might keep its project management platform and integrate it with its ERP solution. A distributor could rely on a best-in-class warehouse management system that connects to the NetSuite platform via application programming interfaces rather than replacing it.

The right question is not “Can the NetSuite platform do this?” but “Is there a better tool for this specific job?” A well-designed technology ecosystem – with NetSuite solutions at the center – can outperform a single platform stretched beyond its natural boundaries.

Actionable steps

✓ Map your core processes first

Before evaluating any system, document what your business actually does end to end. Identify where your pain points live and what outcomes you need to change.

✓ Distinguish core from edge

Separate the processes that belong in your ERP solution, such as financials, supply chain, order management, from those that might be better served by specialized tools, such as field service, advanced planning, e-commerce.

✓ Plan for integration, not isolation

If you use additional tools alongside the NetSuite platform, plan those integrations early. Point-to-point integrations built late in the project are one of the most common sources of scope creep and go-live delays.

✓ Avoid overcustomizing to fill gaps

When NetSuite software does not natively cover a requirement, resist the urge to customize it into something it was not designed to be. Evaluate whether a connected solution might be the cleaner answer.

Focus on business outcomes, not just system features

Every ERP implementation starts with requirements. The most effective ones start with outcomes, and there is a meaningful difference between the two.

A requirements list details what a system must do. An outcome framework denotes what the business must achieve, and it works backward to determine what the system needs to support. This approach, grounded in a jobs-to-be-done (JTBD) framework, keeps implementation teams focused on value rather than features.

Consider a discrete manufacturer deploying a NetSuite implementation to manage production operations. The requirement might be to configure work orders and routing. The outcome is to reduce production cycle time by 20% and eliminate manual scheduling errors. Those two statements lead to very different design choices, and the second one is far more useful when it is time to measure success.

Rather than beginning with what NetSuite software can do, businesses should start with what they must accomplish. Crowe maps every configuration decision to a strategic purpose so new system reflects the business's goals.

Actionable steps

✓ Define outcomes through JTBD analysis

Identify the jobs the business wants the NetSuite platform to do, such as shortening close cycles, improving margin visibility by product line, or accelerating quote-to-cash.

✓ Tie every configuration to an outcome

When design decisions arise, ask whether the choice moves the needle on a defined outcome. If it does not, deprioritize it.

✓ Revisit outcomes at each sprint

Review your outcome list regularly so the build stays aligned with what matters most, as business priorities shift during an implementation.





3

Build toward go-live with iterative sprints

The traditional waterfall approach to ERP – long design phases followed by a single big reveal – is the single greatest predictor of implementation failure. Iterative, sprint-based delivery is the gold standard for a reason.

In a sprint-based model, the team configures a manageable slice of the system, demonstrates it using realistic data, collects feedback, and refines before moving on. This approach surfaces issues early – when they are inexpensive to fix – and keeps business stakeholders engaged throughout the project rather than only at the end.

For a manufacturer, this approach might mean validating the item master, bill of materials structure, and basic work order flow in the first few sprints, long before touching financial consolidation or advanced reporting. For a distribution company, it means confirming that purchase orders, receipts, and vendor payments work correctly before layering in demand planning or multilocation inventory.

The Crowe sprint-based framework is built around this philosophy. Each sprint produces a working, testable slice of the system, not a slide deck or a prototype.

Actionable steps

✓ Sequence sprints by business priority

Start with the processes that are most critical to go-live and most likely to surface design complexity. Do not save hard problems for the end.

✓ Use real data in demos

Understand that stakeholders make better decisions when they see their own customers, items, and transactions in the system. Extract and clean a representative data sample early.

✓ Validate continually, not just at user acceptance testing

Confirm what the team already knows works to avoid presenting an untested system to first-time end users.

✓ Protect the scope baseline

Because sprints naturally generate new ideas, capture them in a backlog after the system goes live rather than absorbing them into the current phase.

Balance technology and people

The most technically sound NetSuite implementation can still fail if the people who need to use it are not ready, willing, or able to do so. Far beyond a soft add-on, change management is a core workflow.

ERP implementations change how people do their jobs. Processes that once lived in spreadsheets, email threads, or tribal knowledge now need to run through a structured system. That shift requires intentional preparation, including communication, training, and leadership alignment, well before go-live.

These factors are especially true for operations-heavy environments. On a manufacturing floor, a production supervisor who does not trust the system might revert to whiteboards and verbal communication within days. In a warehouse, a receiving team that does not understand the new receipt and inspection workflow might create inventory discrepancies that take months to unwind. The system configuration matters, but actual adoption matters more.

Actionable steps

✓ Identify and activate change champions

Identify respected individuals in each department who can model the new behavior, answer peer questions, and surface issues before they escalate.

✓ Communicate early and often

Remember that teams who understand why the change is happening – not just what is changing – adapt faster. Connect the implementation to business outcomes people care about.


✓ Design training around roles, not modules

Train people on the workflows they will actually perform, not on a feature-by-feature tour of the system.

✓ Plan for the first 30 days after go-live

Provide support, monitor process compliance, and address issues quickly before workarounds become habits, because go-live is the beginning of adoption, not the end.



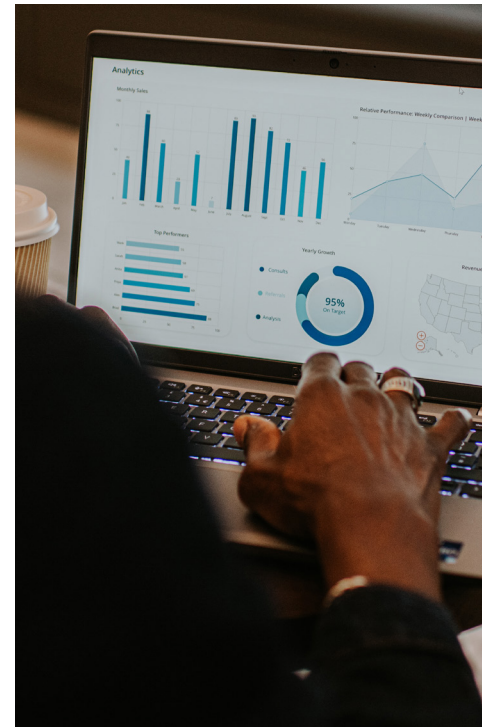

5

Build a data strategy early

Data migration is consistently underestimated, and it's consistently responsible for delayed go-lives. Organizations that treat it as a final step almost always regret it.

The data brought into the NetSuite platform will either accelerate day-one operations or create challenges that hinder long-term success. A clean, well-structured chart of accounts enables meaningful financial reporting from the start. An accurate, complete item master allows purchasing, receiving, and fulfillment to function correctly without manual intervention. Poor data, by contrast, creates a cascade of operational problems that are expensive and time-consuming to fix after go-live.

A strong data strategy covers three things: what data to migrate, how to cleanse and transform it, and who owns its ongoing quality after go-live. For manufacturers, data complexity is especially pronounced. Bills of material, routings, item configurations, and standard costs must be accurate before production orders can be processed reliably. Correctly migrating that data and validating it against the real manufacturing environment are critical actions in the highest risk workstreams in any manufacturing ERP project.

Actionable steps

✓ Start data assessment in week one

Inventory your source systems, understand their data structures, and identify quality issues before the implementation clock starts.

✓ Define governance roles early

Assign clear ownership for data quality by domain, such as items, customers, vendors, chart of accounts, so accountability is established before migration begins.

✓ Run multiple migration cycles

Migrate data early and often into your sandbox environment. Each cycle reveals cleansing gaps that are far easier to resolve before go-live.

✓ Treat data as an asset, not a task

Remember that data quality does not end at go-live. Build processes to maintain it, including duplicate detection, field validation rules, and periodic audits, as part of your operating model.

Prioritize essential capabilities for go-live – then scale

One of the most reliable ways to delay a NetSuite platform go-live is to try to implement everything at once. Scope discipline is not a compromise; it is a strategic imperative.

Every ERP project carries a list of requirements, and not all of them need to be live on day one. The goal of the initial go-live is to run the business reliably and accurately on the new platform. Advanced capabilities, reporting enhancements, workflow automations, and integrations that are valuable but not operationally critical can be sequenced in a structured post-go-live road map.

This principle applies directly to manufacturers. The ability to process purchase orders, receive inventory, issue materials to production, complete work orders, and ship finished goods to customers is paramount. Advanced demand forecasting, machine-level routing optimization, and multiplant consolidation can follow once the foundation is stable.

Crowe helps clients define a minimum viable platform, or a core set of capabilities needed to operate effectively from day one, and builds a phased road map for everything beyond it.

Actionable steps

✓ Define go-live scope in terms of processes, not features

Ask “What processes must run on the NetSuite platform on day one to keep the business operating?” Everything else is a candidate for phase two.

✓ Build the post-go-live roadmap before you go live

Understand that stakeholders accept scope decisions more readily when they can see that deferred items have a plan – not just a promise.

✓ Resist late-stage scope additions

Avoid introducing new requirements in the final weeks before go-live because they are a leading cause of delays and quality issues. Evaluate them against the road map instead.

✓ Measure phase-one success before expanding

Confirm the core platform is stable, adopted, and performing before layering in the next phase of capabilities. go-live is the beginning of adoption, not the end.





7

Treat go-live as the beginning, not the end

Go-live is a milestone, not a finish line. Organizations that treat ERP implementation as a project with a defined end date tend to underinvest in what comes after. Organizations that treat it as a transition into a new operating model can derive substantially more value from the platform over time.

The first 90 days after go-live are among the most important in the entire program. This time period is when process compliance is established or eroded, when data quality issues surface and get resolved or ignored, and when users build confidence in the system or lose it. The decisions made in that window shape how the organization will use its NetSuite implementation for years.

Beyond stabilization, the period after go-live is when the system starts to demonstrate the benefits of investment. Reporting that was not possible before becomes available. Process inefficiencies previously hidden in spreadsheets become visible. Opportunities for automation, integration, and workflow improvement emerge organically as users understand what the system can do.

Our continual performance framework helps organizations sustain this momentum by measuring value creation against the business outcomes defined at the start of the project, supporting ongoing optimization, and helping teams identify what to build next.

Actionable steps

✓ Plan support before go-live

Define who provides support in the first 30 days, how issues are logged and resolved, and what escalation paths exist before you need them.

✓ Monitor process compliance actively

Track whether people are following the designed workflows. Early deviations are easy to correct, but entrenched workarounds are not.

✓ Revisit outcomes at 90 days

Return to the business outcomes defined at the start of the project. Measure what has improved, and identify what has not and why.

✓ Build a continual improvement cadence

Schedule regular reviews of system performance, user feedback, and the post-go-live road map. ERP value compounds over time only if someone is tending it.



Implement confidently with Crowe

Crowe delivers end-to-end NetSuite ERP guidance, from platform evaluation through go-live and continual optimization.

Our certified NetSuite specialists combine deep implementation experience with industry knowledge across manufacturing, distribution, and professional services. Whether you are still deciding if the NetSuite platform is right for your organization or are ready to begin building, Crowe brings the methodology, the tools, and the expertise to help you succeed – on time and on budget.

Connect with Crowe

Ready to take the next step? The Crowe team can help you evaluate your options, build your business case, and execute an implementation that delivers lasting results.



Alejandro Alvarez
Partner, Consulting,
Crowe Advisory LLC
alejandro.alvarez@crowe.com



"Crowe" is the brand name under which Crowe LLP, Crowe Advisory LLC, and their respective subsidiary entities provide professional services. Crowe LLP and Crowe Advisory LLC (and their respective subsidiary entities) practice in an alternative practice structure in accordance with the AICPA Code of Professional Conduct and applicable law, regulations, and professional standards.

Crowe LLP is a licensed independent CPA firm that provides attest services to its clients. Crowe Advisory LLC and its subsidiary entities provide tax, advisory, consulting, and other nonattest services to their clients. Crowe Advisory LLC and its subsidiary entities are not licensed CPA firms. Crowe LLP and Crowe Advisory LLC are independent members of the Crowe Global network. Crowe Global and its member firms, including Crowe LLP and Crowe Advisory LLC, are not a worldwide partnership. Crowe Global and each member firm are separate legal entities. Services are delivered by the member firms. Crowe Global is a Swiss organization and does not render professional services to clients and does not have an ownership interest in Crowe LLP, Crowe Advisory LLC, or any other member firm. Crowe Global and its member firms are not agents of, and do not obligate, one another and are not liable for one another's acts or omissions.

The information contained in this document is not intended to constitute audit, tax, accounting, advisory, consulting, business, financial, investment, legal, or other professional advice and should not be relied upon as such. Some services may not be available to attest clients. The information is general in nature, based on authorities that are subject to change, and is not a substitute for professional advice or services. Before making any decision or taking any action that may affect your business, you should consult a qualified professional adviser. Crowe is not responsible for any loss incurred by any person who relies on the information contained in this document.

For additional information about Crowe LLP, Crowe Advisory LLC, their subsidiary entities, and Crowe Global, please visit <https://www.crowe.com/disclosure>. © 2025 Crowe Advisory LLC. All rights reserved. The Crowe name and logo are trademarks used under license from Crowe Global.
